

# Construction Update



**Lake County**  
**Division of Transportation**  
600 West Winchester Road  
Libertyville, Illinois 60048



**Project:**

## **Miller Rd Improvements**

**Limits:**

Miller Rd from Glen Circle Dr to Biltmore Dr, 0.3 miles east of IL59

**Project Description:**

This project consists of raising the Miller Rd profile and installing a three-span bridge to alleviate road flooding. Other improvements include road resurfacing, construction of a retaining wall, curb and gutter installation, guardrail, drainage, pavement markings and landscape restoration.

---

**Project Status: Active**

**Project % complete: 10%**


### **Current Information:**

Project got underway in late July when Miller Rd was closed to through traffic so that the contractor could begin removing trees and pavement for the construction of the new bridge. The bridge is scheduled to be opened to traffic by October 19 with the remaining work finished by November 30.

The posted detour uses IL59 to IL22 to US12 according to the attached map. LCDOT coordinated with IDOT so that the resurfacing of IL22 within the detour limits of IL59 to US12 will be deferred until after October 19 when Miller Rd reopens. IDOT's resurfacing project will continue west of IL59 to US14 in August & September.

A field office for the Miller Rd project was just set up and a phone number for questions is now available - see contact info in the right column. Utilities have all been relocated and the contractor is currently driving piles into the ground for the new bridge.

*Project Location:*

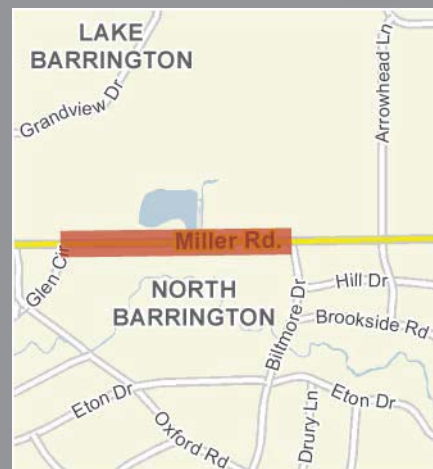

*Construction Information Contact:*

**Jeff Dayson, Resident Engineer**  
**847.381.1547**

*Additional Contact(s):*

**Glenn Petko, LCDOT**  
**Engineer of Construction**  
**847.377.7400**

**Al Giertych, LCDOT**  
**Assistant County Engineer**  
**847.377.7400**

*Lake County Traffic Information:*  
**lakecountypassage.com**

*Date:* **8/13/13**
