

# Construction Update



**Lake County**  
**Division of Transportation**  
600 West Winchester Road  
Libertyville, Illinois 60048



## Project:

### **Delany Road Reconstruction and Widening**

## Limits:

North of Sunset Av (Tannahill Dr) to north of Wadsworth Rd (Oak Knoll Rd)

## Project Description:

Existing Delany Rd pavement will be reconstructed and widened to five lanes, with two through lanes in each direction. New traffic signals will be installed at York House Rd, Wadsworth Rd and Continental Dr with left turn lanes all around and select right turn lanes as warranted by traffic volume. This is actually two contracts with the same contractor, split just north of York House Rd.

**Project Status: Active**

**Project % complete: 40%**


## Current Information:

Following a challenging 2012, which consisted of limited roadwork due to numerous utility conflicts, we anticipate improved progress for 2013. Delany Rd north of York House Rd is planned to finish by October 2013 and the southern portion may finish by the end of 2013 or carry over into spring of 2014.

The northern half of the project had gas company relocations in progress all winter, we do not anticipate any further utility conflicts that will delay our work. The permanent pavement on the western third of Delany Rd and the northern third of Wadsworth Rd were constructed last year. Our next stage this spring will be construction of the middle third on both roads, then move traffic onto the new pavement by early summer, while we complete the eastern third of Delany Rd and southern third of Wadsworth Rd.

The southern half of the project will begin in the spring as weather allows, by moving traffic onto the temporary pavement on the east side of Delany Rd while the western third is built. By summer we would like to switch traffic into a split configuration where southbound Delany Rd and eastbound York House Rd will use the new pavement, while the middle third of each road is constructed. Then late in the year, the plan is to move traffic all onto new pavement while the remaining thirds are constructed on the east side of Delany Rd and north side of York House Rd.

## Project Location:

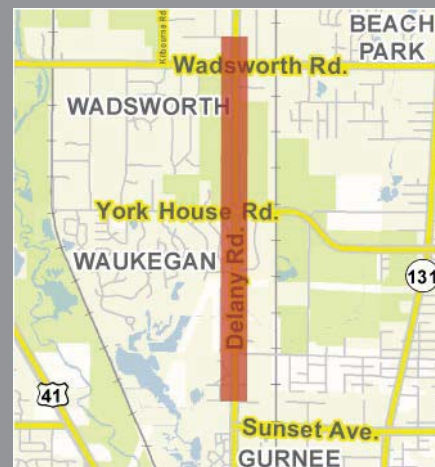

## Construction Information Contact:

Jennifer Grazier, Ciorba Consulting  
Resident Engineer  
847.672.8766

## Additional Contact(s):

Glenn Petko, LCDOT  
Engineer of Construction  
847.377.7400

Al Giertych, LCDOT  
Assistant County Engineer  
847.377.7400

## Lake County Traffic Information:

**lakecountypassage.com**

Date: 4/2/13
